
**Hilt — implemented MongoDB schema**
**Current checkout · 9 November 2026**

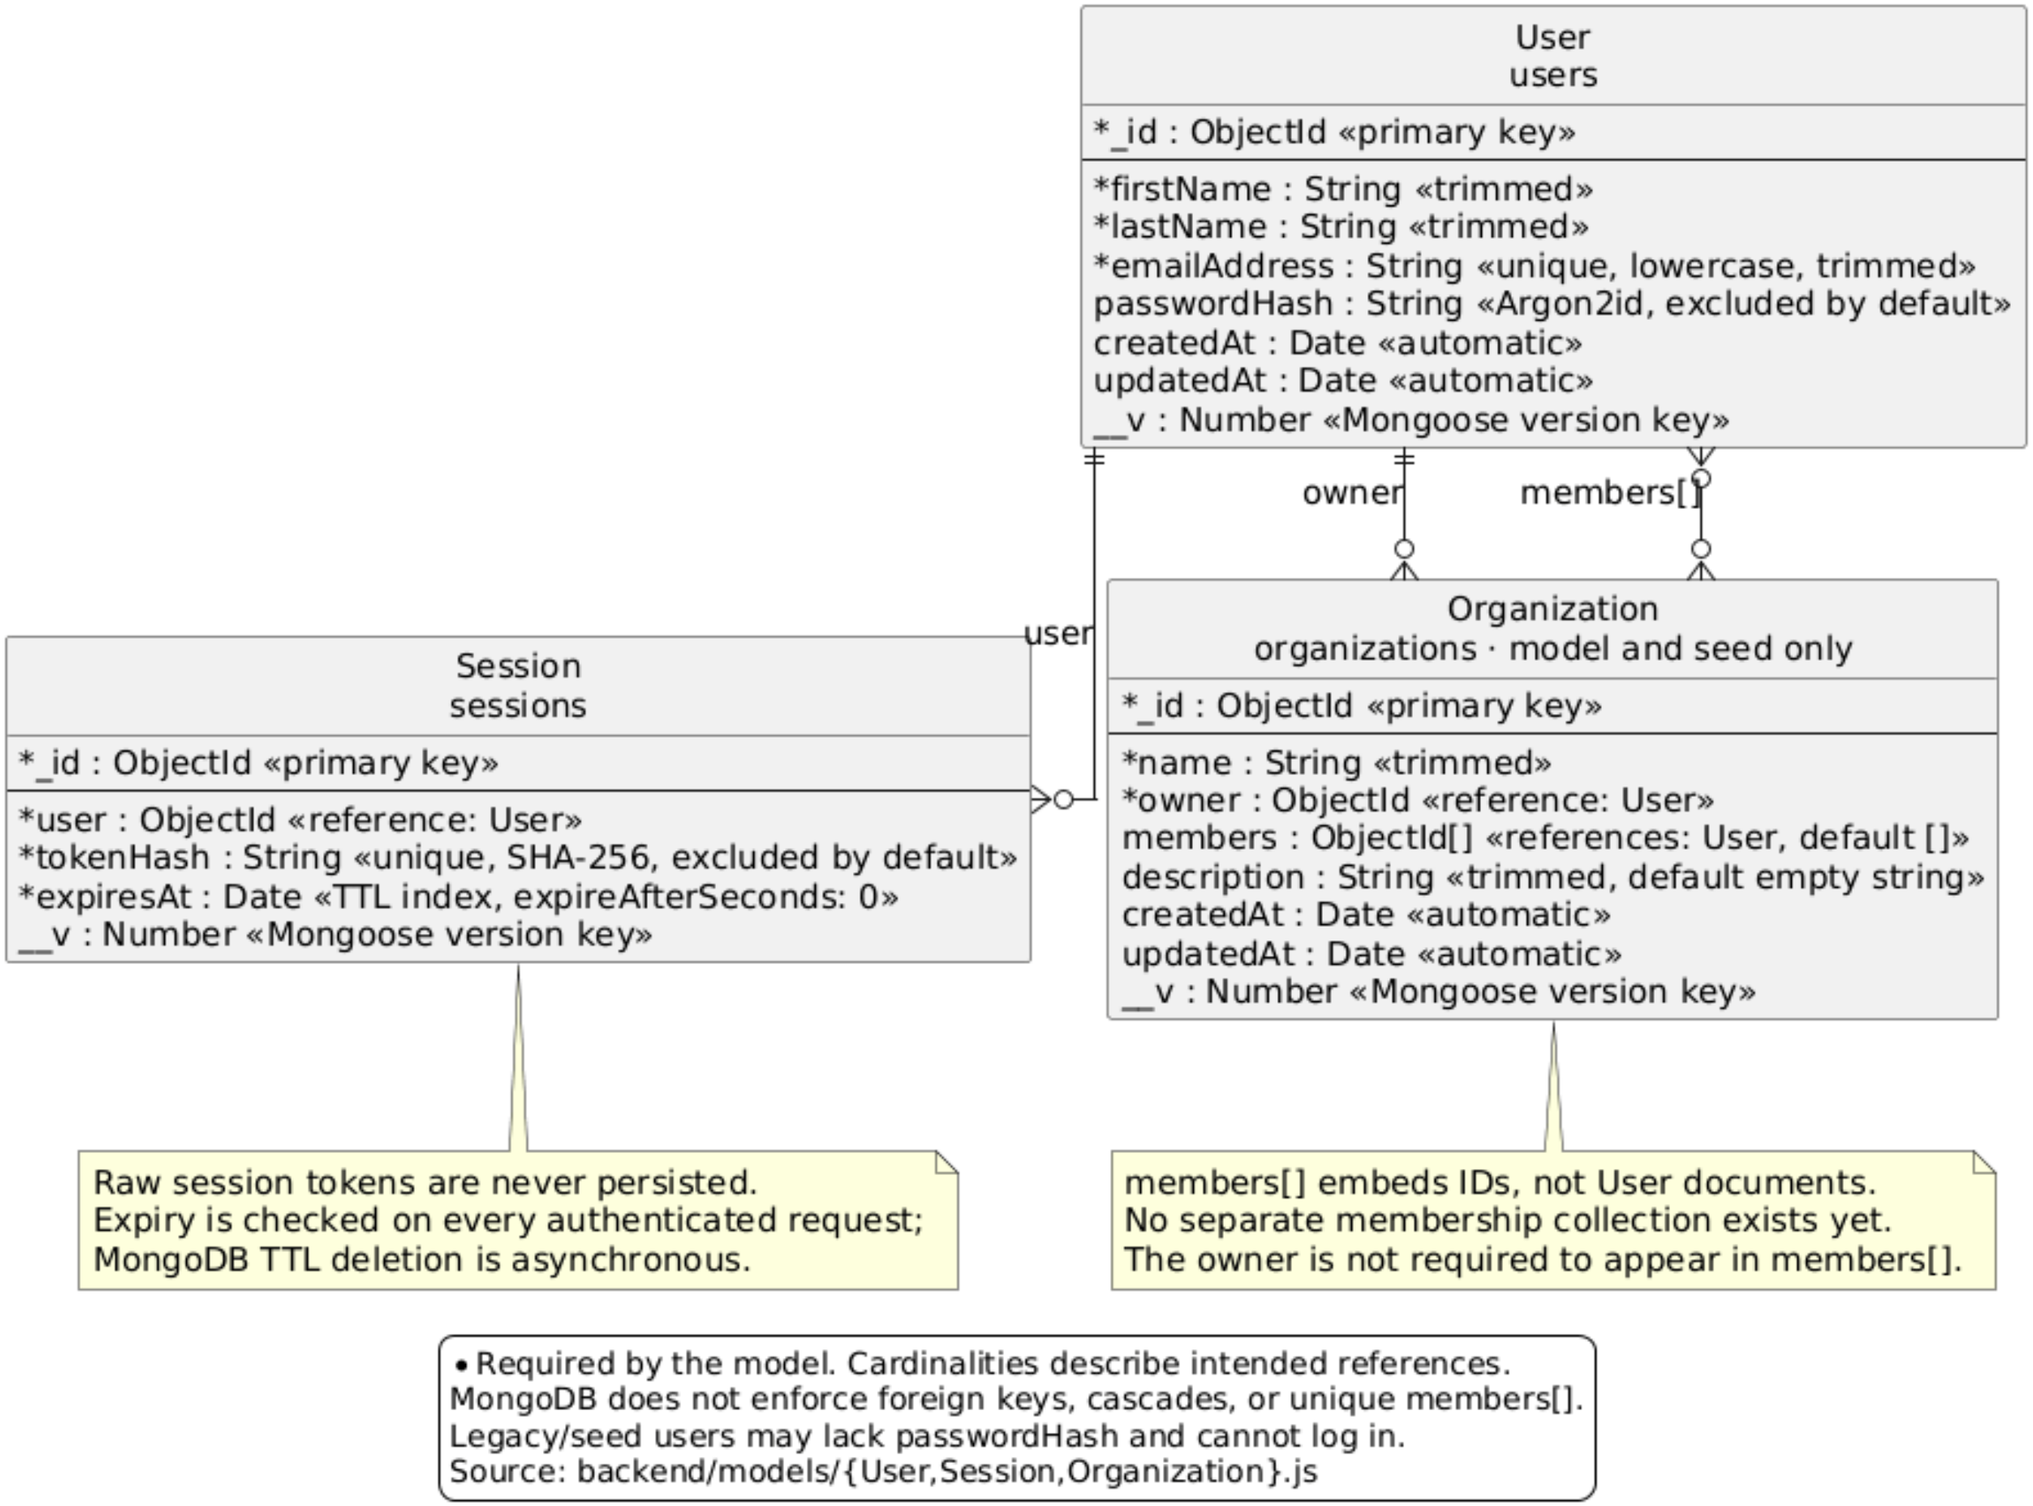


**Hilt - presentation delivery plan**
**Status: 9 November 2026 | Presentation submission due: 20 November 2026**

| Start | End | Th 22 | Fr 23 | Sa 24 | Su 25 | Mo 26 | Tu 27 | We 28 | Th 29 | Fr 30 | Sa 31 | Su 1 | Mo 2 | Tu 3 | We 4 | Th 5 | Fr 6 | Sa 7 | Su 8 | Mo 9 | Tu 10 | We 11 | Th 12 | Fr 13 | Sa 14 | Su 15 | Mo 16 | Tu 17 | We 18 | Th 19 | Fr 20 |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | | October 2026 | | | | | | | | | | | | | | | | | | November 2026 | | | | | | | | | | | |
| | | – Recorded evidence (milestones, not hours worked) ——— | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Oct 22 | Oct 22 | ◆ Scaffold, Docker, models - Ishfaq | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Oct 24 | Oct 24 | | | ◆ PRD draft - Alexander | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Oct 29 | Oct 29 | | | | | | | | ◆ Auth API commit - Alexander | | | | | | | | | | | | | | | | | | | | | |
| Nov 6 | Nov 6 | | | | | | | | | | | | | | | | ◆ Minimal auth UI / live disposable-account check | | | | | | | | | | | | | | |
| Nov 9 | Nov 9 | | | | | | | | | | | | | | | | | | | ◆ Approved profile rollout / live persistence check | | | | | | | | | | |
| Nov 9 | Nov 9 | | | | | | | | | | | | | | | | | | | ◆ Club workflows, routed web, cookie sessions / live checks | | | | | | | | | | |
| | | – Current work / known check-in ——— | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Nov 9 | Nov 9 | | | | | | | | | | | | | | | | | | | ■ ERD, Gantt, own-profile workflow; verification | | | | | | | | | | |
| Nov 9 | Nov 9 | | | | | | | | | | | | | | | | | | | ◆ Team 2 check-in; upload beforehand | | | | | | | | | | |
| | | – Remaining implementation window (owners unassigned) ——— | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Nov 9 | Nov 18 | | | | | | | | | | | | | | | | | | | ■ University verification and recovery - email server blocked | | | | | | | | | | |
| Nov 9 | Nov 18 | | | | | | | | | | | | | | | | | | | ■ Events, RSVP, calendar; API tests and contracts | | | | | | | | | | |
| Nov 9 | Nov 18 | | | | | | | | | | | | | | | | | | | ■ Custom roles; authorization and invariants | | | | | | | | | | |
| Nov 9 | Nov 18 | | | | | | | | | | | | | | | | | | | ■ Page editor, safe assets, visibility, shared rendering | | | | | | | | | | |
| Nov 9 | Nov 18 | | | | | | | | | | | | | | | | | | | ■ Attendance, QR, staff and self check-in | | | | | | | | | | |
| Nov 9 | Nov 18 | | | | | | | | | | | | | | | | | | | ■ Inbox, announcements, reminders, push/email/Discord | | | | | | | | | | |
| Nov 9 | Nov 18 | | | | | | | | | | | | | | | | | | | ■ Moderation, recoverable audit, preview and restore | | | | | | | | | | |
| Nov 9 | Nov 18 | | | | | | | | | | | | | | | | | | | ■ OAuth, React Native, web/mobile parity and integration | | | | | | | | | | |
| | | – Presentation preparation and submission ——— | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Nov 9 | Nov 19 | | | | | | | | | | | | | | | | | | | ■ Diagrams, slides, contributions and AI disclosure | | | | | | | | | | |
| Nov 16 | Nov 19 | | | | | | | | | | | | | | | | | | | | | | | | | | ■ API acceptance, Lighthouse, release checks and rehearsal | | | | |
| Nov 20 | Nov 20 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | ◆ MERN presentation submission due - course deadline | |
| | | Th 22 | Fr 23 | Sa 24 | Su 25 | Mo 26 | Tu 27 | We 28 | Th 29 | Fr 30 | Sa 31 | Su 1 | Mo 2 | Tu 3 | We 4 | Th 5 | Fr 6 | Sa 7 | Su 8 | Mo 9 | Tu 10 | We 11 | Th 12 | Fr 13 | Sa 14 | Su 15 | Mo 16 | Tu 17 | We 18 | Th 19 | Fr 20 |
| | | October 2026 | | | | | | | | | | | | | | | | | | November 2026 | | | | | | | | | | | |

Green: dated evidence. Blue: current local work. Purple: check-in / course deadline.
Orange: proposed work windows; owners and individual feature durations are unassigned.
Implementation rows share the remaining window; they are not separate effort estimates.
Deadline source: Course Calendar and instructor announcement of 2 November 2026.
Presenting starts the week of 30 November; Team 2's slot is not yet assigned.
Email delivery remains blocked. Payment processing remains stretch scope.

**Hilt — proposed PRD data relationships**
**PLANNED · not the implemented database schema**

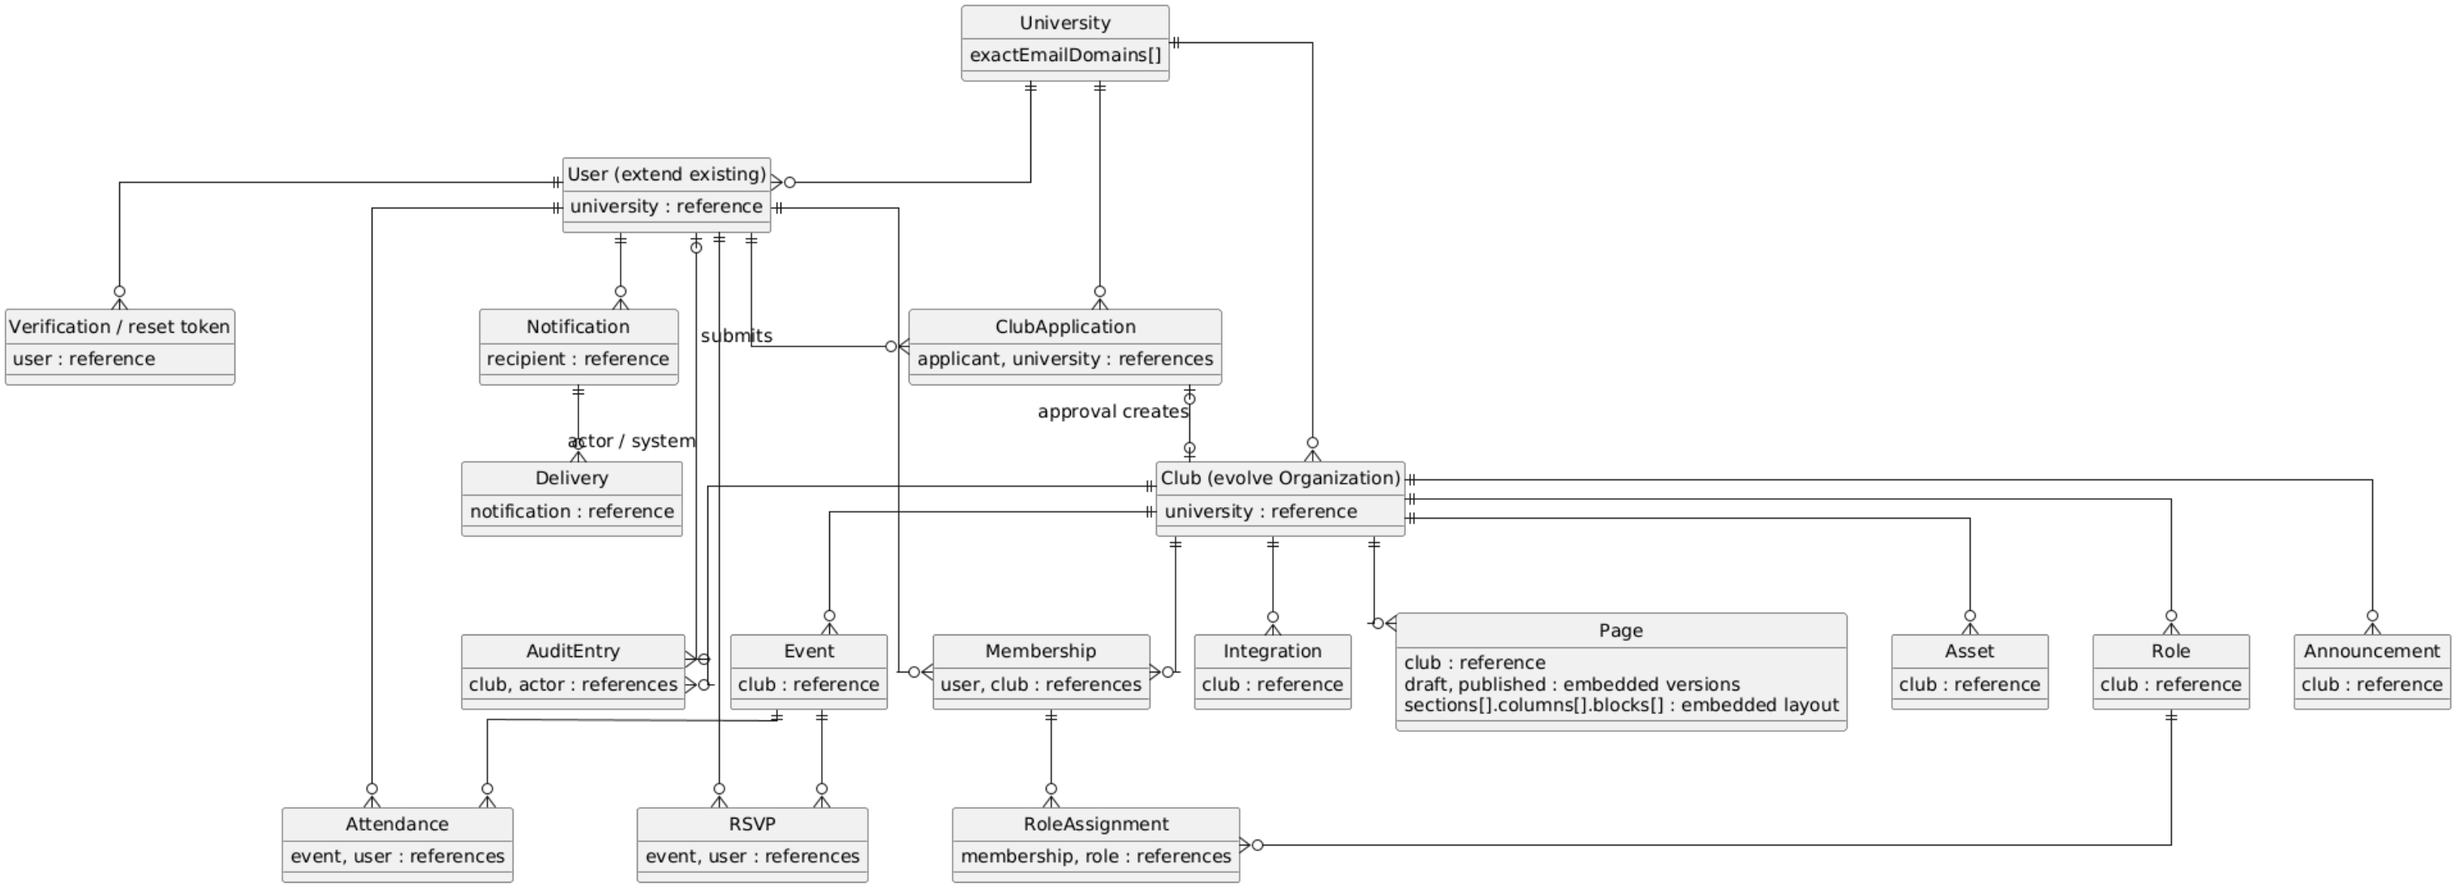


Proposed logical relationships from docs/prd.md; fields and indexes remain to be designed.
References use IDs; only Page layout/version content is proposed as embedded here.
Membership, RSVP, and Attendance remain independent records.
Event blocks reference Event; using a block never duplicates RSVP/Attendance.
Audits must retain recoverable prior state; delivery history survives recovery.
Not a migration or a claim that these collections or APIs exist.
